ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**COLIVING LAURELES-ESTADIO**	**66 days**	**Mon 1/1/24**	**Mon 4/1/24**	
2		**Obras Preliminares**	**10 days**	**Mon 1/1/24**	**Fri 1/12/24**	
3		Demolición de muros, baños, cocina y escaleras	10 days	Mon 1/1/24	Fri 1/12/24	
4		**Acabados**	**51 days**	**Mon 1/15/24**	**Mon 3/25/24**	
5		Construcción de muros en mampostería	15 days	Mon 1/15/24	Fri 2/2/24	3
6		Construcción de cocina social	15 days	Mon 1/15/24	Fri 2/2/24	3
7		Construcción de acabados de piso en SPC	10 days	Mon 2/5/24	Fri 2/16/24	5,6
8		Enchape para baños	12 days	Mon 2/5/24	Tue 2/20/24	5
9		Pintura de muros nuevos y existentes	10 days	Tue 3/12/24	Mon 3/25/24	27
10		**Carpintería en madera**	**10 days**	**Mon 2/19/24**	**Fri 3/1/24**	
11		Closet para habitaciones	10 days	Mon 2/19/24	Fri 3/1/24	7
12		Puertas interiores	10 days	Mon 2/19/24	Fri 3/1/24	7
13		Puerta principal	10 days	Mon 2/19/24	Fri 3/1/24	7
14		Vidriera Balcón	10 days	Mon 2/19/24	Fri 3/1/24	7
15		**Carpintería metálica**	**30 days**	**Mon 2/5/24**	**Fri 3/15/24**	
16		Ventanas para habitaciones	15 days	Mon 2/5/24	Fri 2/23/24	5
17		Claraboyas para habitaciones	5 days	Mon 2/26/24	Fri 3/1/24	16
18		Pérgola para salón múltiple	10 days	Mon 3/4/24	Fri 3/15/24	17
19		Puerta vidriera para garage	5 days	Mon 3/4/24	Fri 3/8/24	14
20		**Instalaciones hidrosanitarias**	**26 days**	**Mon 2/5/24**	**Mon 3/11/24**	
21		Instalaciones de redes hidrosanitarias para baño	10 days	Mon 2/5/24	Fri 2/16/24	5
22		Sanitario	5 days	Wed 2/21/24	Tue 2/27/24	21,8
23		Ducha	2 days	Wed 2/28/24	Thu 2/29/24	22
24		Lavamanos	5 days	Fri 3/1/24	Thu 3/7/24	23
25		Accesorios de baño	2 days	Fri 3/8/24	Mon 3/11/24	24
26		**Instalaciones eléctricas**	**10 days**	**Tue 2/27/24**	**Mon 3/11/24**	
27		Instalaciones de redes eléctricas global	10 days	Tue 2/27/24	Mon 3/11/24	5,20FF
28		**Mobiliario**	**35 days**	**Tue 2/13/24**	**Mon 4/1/24**	
29		Compras	30 days	Tue 2/13/24	Tue 3/26/24	30SF
30		Instalación de mobiliario	5 days	Tue 3/26/24	Mon 4/1/24	9

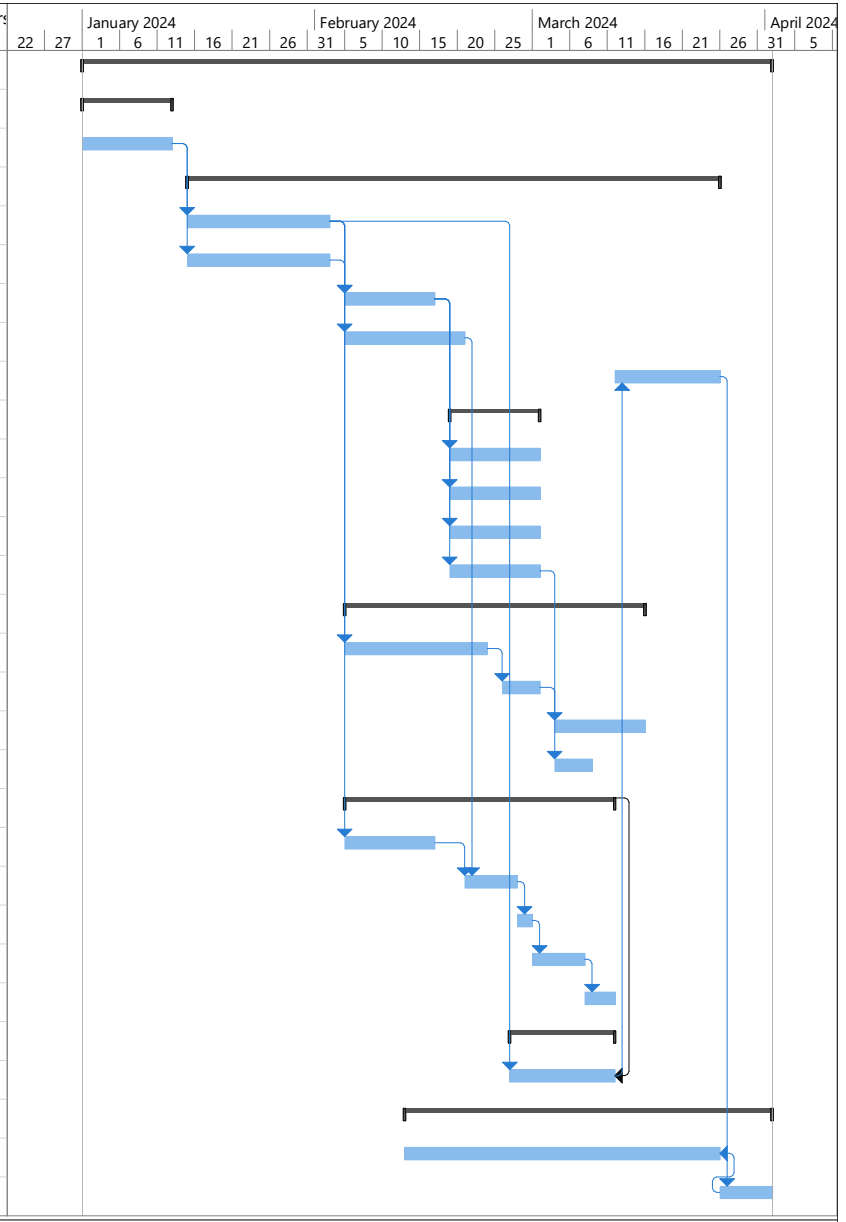

Project: Cronograma Coliving
Date: Wed 8/16/23

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
